

Work Order ID 141202

Monday, February 01, 2016 7:47:46 AM

141202

Page 1

Item ID: D6104-007 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Round Billet, 17-4
 Start Date: 2/1/2016 Start Qty: 10.00 ***10*** Cust Item ID:
 Required Date: 2/8/2016 Req'd Qty: 10.00 ***10*** Customer:
 Reference:

Approvals: Process Plan: MCS Date: FEB 01 2016 Tooling: Date: Run Start ***NR1***
 QC: Date: SPC (Y/N): Date: Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D6104	Rev B								

100 PURCHASING 0.00 ***100*** 10 FEB 01 2016 **DAS 13 9-99**

Purchasing Memo
 Purchasing Issue P/O: 31199
 a) Description: S.S round billet
 b) Ø4.50" x 5.10" long
 c) Tolerance on all dimensions are +0.030"/-0.000"
 d) Material: 17-4PH Stainless steel (Ams 5643 or Aisi 630)
 e) One blank makes 2 parts
 f) Material certification required

110 Receive & Inspect for Damage & Mat'l Certs 0.00

110 Packaging Memo 0.00
 Packaging Ensure material certification is attached

FEB 08 2016 10

DAS 6 9-99

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Work Order ID 141202

Monday, February 01, 2016 7:47:46 AM

141202

Page 2

Item ID: D6104-007

Accept

N1900040100

Setup Start

NS1

Revision ID:

Item Name: Round Billet, 17-4

Stop

NS2

Start Date: 2/1/2016 Start Qty: 10.00

10

Cust Item ID:

Required Date: 2/8/2016 Req'd Qty: 10.00

10

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

120

QC18 In-Coming Inspection Material

0.00

120

QC

Memo

0.00

Quality Control

Ensure Material certification comply to Dwg D6104

DAS
14
9-09

16/02/09

130

Identify as per dwg & Stock Location: **MAT043** 0.00***130***

Packaging

Memo

0.00

Packaging

DAS
14
9-09

16/02/09

140

QC21- Final Inspection - Work Order Release 0.00

140

QC

Memo

0.02

Quality Control

FEB 09 2016

MLS

SMA 20160209

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval	
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
		OTHER :							

Picklist Print

Monday, February 01, 2016 7:47:49 AM

Page 1

Work Order ID: 141202

141202

Parent Item: D6104-007

D6104-007

Parent Item Name: Round Billet, 17-4

Start Date: 2/1/2016

Required Date: 2/8/2016

Start Qty: 10.00

Required Qty: 10.00

Comments: IPP A: 01.05.08New Issue EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D6104-007P		Purchased	No			110	Each	0.0000	1	10			

D6104-007P

17-4 SS Roundbar 4.50"Od

**

DAS
6
9-89

FEB 08 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QS1042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER :			
Misidentified ☐	Past Due ☐																																																																




DESIGN 		DRAWN BY 		DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED 		APPROVED 		DRAWING NO. Rev. B D6104 SHEET 1 OF 1	
DATE 02.11.25			TITLE SCALE ROUND BILLET, 17-4 NTS		
A	01.04.10		NEW ISSUE		
B	02.11.25		CLARIFY ALLOY SPEC ADDED D6104-009/-011 REDUCE LENGTH OF BILLETS		

RELEASED

02.11.29

SPECIFICATION CONTROL DRAWING

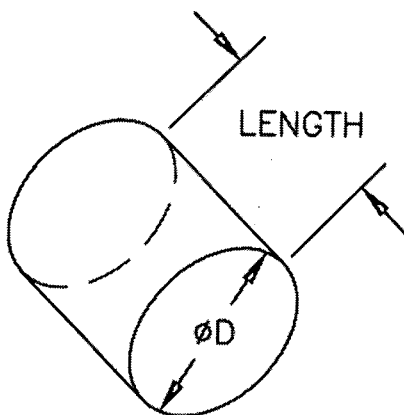

copy
VIO
141202-01
1602-01

MATERIAL: 17-4 PH SS (AMS 5643 OR AISI 630) MIN UTS = 170 KSI (38 HRC)

PURCHASE MATERIAL ACCORDING TO THE FOLLOWING TABLE. SPECIFY ALLOY, DIAMETER X LENGTH (+0.030/-0.000) AS SHOWN.

TOLERANCE ON ALL DIMENSIONS IS +0.030/-0.000.

ALL DIMENSIONS ARE IN INCHES

Part No.	Alloy	D (Diameter)	Length
D6104-001	17-4 PH STAINLESS STEEL	Ø3.00	3.80
D6104-003	17-4 PH STAINLESS STEEL	Ø3.25	3.80
D6104-005	17-4 PH STAINLESS STEEL	Ø4.00	5.10
D6104-007	17-4 PH STAINLESS STEEL	Ø4.50	5.10
D6104-009	17-4 PH STAINLESS STEEL	Ø5.25	4.10
D6104-011	17-4 PH STAINLESS STEEL	Ø6.50	4.10

Copyright © 2001 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong				
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions				
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance				
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect				
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing				
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved				
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing				
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish				
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread				
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence				
Past Expiry Date ☐	☐ Manufacturing Process	OTHER :							
Misidentified ☐	☐ Past Due								



Castle Metals®

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 2 of 2

120329630	NORTH AMERICAN STAINLESS			10			236.4263
-----------	--------------------------------	---	--	----	--	--	----------

These commodities/technologies are subject to US Export Administration & US State Dept. Regulations and, if intended for export, were/are exported thereunder. Diversion contrary to US Law is Prohibited.

We hereby certify the material covered by this certification conforms in accordance with the above specifications and has been found to meet the applicable requirements for the material, including any specifications forming a part of the description. Test reports are on file subject to examination. All claims for defective material are waived unless made in writing to A.M. Castle & Co. within 60 days of the shipment. Material cut to the correct size, or material cut by the customer cannot be returned for credit.

Reviewed by Authorized Castle Metals Representative:

Date:

Name:

Amelia A. Johnson

FEB 04 2016



HEAT NUMBER
MECHANICAL ID
ITEM CODE
LOT NUMBER
PO NUMBER
RECEIPT DATE
SUPPLIER
SPECIFICATION
LCS
COMMENT
APPROVED

Castile Metals FP
N 516
14998
294342
9-26-14
NHS
y



**NORTH AMERICAN
STAINLESS**

METALLURGICAL TEST REPORT

6870 Highway 42 East
Ghent, KY 41045-9615
(502) 347-6000

Certificate: 990028 07 Mail To:
A.M. CASTLE AND COMPANY
1420 KENSINGTON ROAD-SUITE 220
OAK BROOK IL 60523

Customer: 0032 001
NAS Order: LP 23209 1
Your Order: 294342 Item Code: 14998

Ship To:
A.M. CASTLE AND COMPANY
3400 NORTH WOLF ROAD
FRANKLIN PARK IL 60131

Date: 9/23/2014 Page: 1 Of 1
Steel: 630(17-4)
Finish: Hot Finish
Dia/Thk: 4.5000 in
Leg Length:
Length: 144.00 in
Corrosion:

PRODUCT DESCRIPTION:

AMS 2303E, AMS 5643E
Round Bar, Hot Rolled, Annealed, Rough Turned
UNS S17400, EN 10204 3.1, ASTM A484/11, MACRO OK, AMS 5643T
ASTM A564/10, AMS 2303, ASME SA564-07, ASTM F899/11 (CHEM ONLY)
SOL. ANNEALED @ 1900F MIN FOR 1 HR MIN. and air cooled to RT
H900 MECH. PROPERTIES ARE CAPABILITY ONLY*

REMARKS:

COMPLIES W/REQUIREMENTS OF DFAR 252.225-7009 EU DIRECTIVE
2011/65/EU. RoHS. EAF+AOD+CC. NO WELD REPAIR. MELTED AND MFG
IN USA FREE FROM MERCURY AND LOW MELTING ALLOY CONTAMINATION

DAS

14
9-89 16/02/09

Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight	Bundle Weight
BG61761	2582								

CHEMICAL ANALYSIS CM(Country of Melt) ES(Spain) US(United States) ZA(South Africa) JP(Japan) Chemical Analysis per ASTM A751/08

Heat	Supplier #	CM	C %	CB %	CO %	CR %	CU %	MN %	MO %	N %	NI %	P %
W5T6		US	.016	.286	.10	15.14	3.07	.77	.14	.036	4.43	.025
			S %	SI %	TA %	TI %						
			.0225	.39	.0050	.0020						

MECHANICAL PROPERTIES

	Id	HB	Grain	Ferrite	TS-900CAP	YS-900CAP	EL-900CAP	RA-900CAP	RC-900CAP	FREQ.	SEV.
	No.	No.	No.	%	KSI	KSI	% 4D	%	No.	No.	No.
BG61761	R L	321.0	7.0	.80	196.11	173.92	13.38	43.95	41.5	.17	.10

NAS hereby certifies that the analysis on this certification is correct. Based upon the results and the accuracy of the test methods used, the material meets the specifications stated. These results relate only to the items tested and this report cannot be reproduced, except in its entirety, without the written approval of NAS

Technical
Dept. Mgr.

AB Bhavs

ABHIJEET BHAVE



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

PURCHASE ORDER

Purchase Order ID PO31199

Purchase Order Date 2/1/2016

PO Print Date 2/1/2016

Page Number 2 of 2

Order From :

METAUX CASTLE
P.O. BOX 4090 STN A
TORONTO, ONTARIO M5W OE9
CANADA

VU-MET002

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

Ship To Contact

Ship To Phone

Ship Via:

Yours ppd

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax #

10127-2607

Terms

Net 30

Currency

USD

FOB

Destination-Collect

Line Total:

\$705

3 D6104-007P

17-4 SS Roundbar 4.50"Od

2/15/2016

10.00

Yes

Each

\$68.53

\$685.

2/15/2016

AS PER DWG D6104 REV. B
B141202

MATERIAL: 17-4 PH AS PER AMS 4643 OR AISI 630
SIZE: 4.50" X 5.10" LONG

16/2/8

Line Total:

\$685.3

4 71401-45

procurement quality clauses

2/15/2016

1.00

No

\$0.00

\$0.00

2/15/2016

Procurement Quality Clauses

A005 right of entry

A012 chemical and physical test report

A016 personnel qualification

A017 raw material identification

A026 certification of material conformance

A041 quality management system

A042 dart notification by supplier

A043 retention of quality documents

Line Total:

\$0.00

PO Total:

\$2,466.30

Note: Terms & Condition of Purchasing(Suppliers) and Procurement Quality Clauses are an integral part of our AS9100 requirements. To learn in detail, please visit www.dartaerospace.com for further explanation.

Change Nbr:

1

Change Date: 2/1/2016

**Castle Metals®**

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 1 of 2

Shipment No:2873242

Ship From: A. M. CASTLE & CO. 2150 ARGENTIA ROAD MISSISSAUGA, ON L5N 2K7 CAN		Sold To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA		Ship To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CAN		Deliver To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA									
Date Shipped 04-FEB-16		F.O.B. ORIGIN		Freight Terms Prepaid		Carrier MANITOULIN		BOL No 2873242-2							
Shipment Details					Final Destination Branch - TOR										
Order No 4235967		Line No 1		Item No 14998.MO <i>16/2/18</i> <i>SD</i>		Description 4.5000.RD.17CR-4NI.STAINLESS.RT.SOL TR.COND A.132.0000-156.0000 CUT TO 5.1 IN (+ .1250/- .0000 IN) - BAND SAW CUTTING SPECIFICATIONS: AMS 5643 ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #'S Email P/s and certs to: clavoie@dartaero.com									
Purchase Order No 31199		Part Number YOUR ITEM NUMBER: D6104-007		Ordered Qty 10.00 PCS			Invoice Qty 10.00 PCS								
Details		USE HEAT # N5T6 ONLY ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #'S Email P/s and certs to: clavoie@dartaero.com END USER: DART AEROSPACE END USE: COMMERCIAL AIRCRAFT PARTS													
Delivery No.		Mill		Heat Number		Mech Id		PCS		Width (IN)		Length (IN)		Shipped Qty(LBS)	

MATERIAL RECEIPT INSPECTION FORM

MATERIAL: D6104-007
DATE: 16/02/09

PO / BATCH NO.: 31199/141202

MATERIAL CERT REC'D: yes
QUANTITY RECEIVED: 10
QUANTITY INSPECTED: 10
QUANTITY REJECTED: _____

THICKNESS ORDERED: 04.500 X 5.10
THICKNESS RECEIVED: 4.520 X 5.225
SHEET SIZE ORDERED: _____
SHEET SIZE RECEIVED: _____

DESCRIPTION	NCR (Check Y/N)	COMMENTS
SURFACE DAMAGE	Y ☒ N ☐	
CORRECT FINISH	☒ Y ☐ N ☐	
CORROSION	Y ☐ N ☒	
CORRECT GRAIN DIRECTION	☒ Y ☐ N ☐	
CORRECT MATERIAL	☒ Y ☐ N ☐	
CORRECT THICKNESS	☒ Y ☐ N ☐	
PHOTO REQUIRED	Y ☐ N ☒	
CORRECT MATERIAL	☒ Y ☐ N ☐	
CORRECT REF # TO LINK CERT	☒ Y ☐ N ☐	
CORRECT MATERIAL IDENTIFICATION	☒ Y ☐ N ☐	
CORRECT M# ON THE MATERIAL	☒ Y ☐ N ☐	
DOES THIS MATERIAL REQUIRE ENGINEERING SIGN OFF	Y ☐ N ☒	
DOES THIS REQUIRE AN EXTRUSION REPORT	Y ☐ N ☒	

CUT SAMPLE PIECE OF MATERIAL AND PREFORM A HARDNESS CHECK. RECORD RESULTS BELOW				
TYPE OF MATERIAL	HRC	HRB	DUR A	DUR D
SIZE OF TEST SAMPLE				
HARDNESS / DUROMETER READING				

testers located in the Quality Office

QC 18 INSPECTION	ENGINEERING SIGNOFF (if required)
INSPECTED BY: <u>14</u> <u>9-99</u>	SIGNED OFF BY: _____
DATE: <u>16/02/09</u>	DATE: _____

Attach this inspection sheet with the corresponding material cert and remit to be scanned and received in

MATERIAL RECEIPT INSPECTION FORM

INSTRUCTIONS FOR INSPECTING BAR, TUBING, ROUND, & SHEET STOCK

- 1- VERIFY STOCK TO DART PURCHASE ORDER
- 2- MEASURE ALL DIMENSIONS FOR EACH PURCHASED STOCK
 - a. WIDTH, THICKNESS, DIAMETER, WALL THICKNESS & LENGTH
- 3- VERIFY CONDITION OF MATERIAL i.e. DAMAGED, CORRODED, etc.
- 4- VERIFY THAT SUPPLIER HAS A NUMBER (HEAT #) ON ITS RECEIVING REPORT TO LINK TO MATERIAL CERTS
- 5- VERIFY MATERIAL CERTS ARE CORRECT TO THE DART PO INSTRUCTIONS
- 6- REMOVE / CUT A PIECE OF MATERIAL FOR SAMPLE HARDNESS TESTING

INSTRUCTIONS FOR INSPECTING SKIDTUBE & STEP EXTRUSION

- 1- VERIFY TO DART SUPPLIED DRAWING
 - 2- SAMPLE INSPECT MATERIAL IN BUNDLE TO ENSURE MATERIAL CAN BE RECEIVED INTO DART
 - 3- USING PORTABLE HARDNESS TESTER VERIFY HARDNESS OF THE MATERIAL TO THE DRAWING
 - 4- VERIFY THAT MATERIAL CERTS MATCH TO WHATS CALLED UP ON THE DART DRAWING
- AFTER MATERIAL PASSES INSPECTION**
- 5- HAVE DART EMPLOYEES START STOCKING MATERIAL BUT REQUEST MIN 20pcs FOR FULL INSPECTION
 - 6- INSPECT ALL DIMS AS PER DRAWING REQUIREMENTS

INSTRUCTIONS FOR INSPECTING CROSS TUBE MATERIAL

- 1- VERIFY MATERIAL CERTS MATCH THE REQUIREMENTS ON THE DART DRAWINGS
- 2- INSPECT MIN. HALF THE BATCH OF EXTRUSION RECEIVED INTO DART
- 3- INSPECT MATERIAL AS PER THE EXTRUSION REPORT
 - a. WALL THICKNESS USING ULTRA-SONIC IN 4 LOCATIONS
 - b. OUTSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - c. INSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - d. STRAIGHTNESS @ CENTER OVER 12" SPAN
 - e. WALL THICKNESS USING TUBE MICROMETER HIGHEST/LOWEST BOTH ENDS
- 4- IDENTIFY EACH TUBE IN SEQUENCE OF INSPECTING (TUBE 1, TUBE2.....) AND W/O# AND PO#
- 5- RECORD ALL FINDINGS ON EXTRUSION REPORT

IF ANY QUESTIONS PLEASE SEE QC COORDINATOR BEFORE GOING FURTHER
